

Construction Update

Devonport Town Centre | Safety Improvements

On behalf of everyone at Auckland Transport we hope this newsletter finds you and your whānau well.

We are nearing the completion of major construction works for Devonport Town Centre.

For this final newsletter issue, we would like to share the safety improvements we've delivered since construction began on 12 June 2023 and what we have left to do. Photos of the completed works begin on page 3. The list of remaining works is on page 6.

We would like to thank the community for your patience while we've carried out this important safety work. We also acknowledge everyone who shared their views with AT including representatives from the community, Business Association, Bike Auckland, Devonport-Takapuna Local Board and Ward Councillors.

For regular updates, please visit our website:

[AT.govt.nz/devonportsafespeeds](https://at.govt.nz/devonportsafespeeds)

or scan the QR code.




Victoria Road and King Edward Parade
Safety Improvements



What we are doing

We will be building raised crossings, a separated cycleway, upgrading streetlighting at pedestrian crossings, minor footpath upgrades, and making other safety improvements around the area.

These improvements will slow down traffic to create an environment that is safer for everyone. Check out our staging map below that shows how we will be constructing our safety improvements.

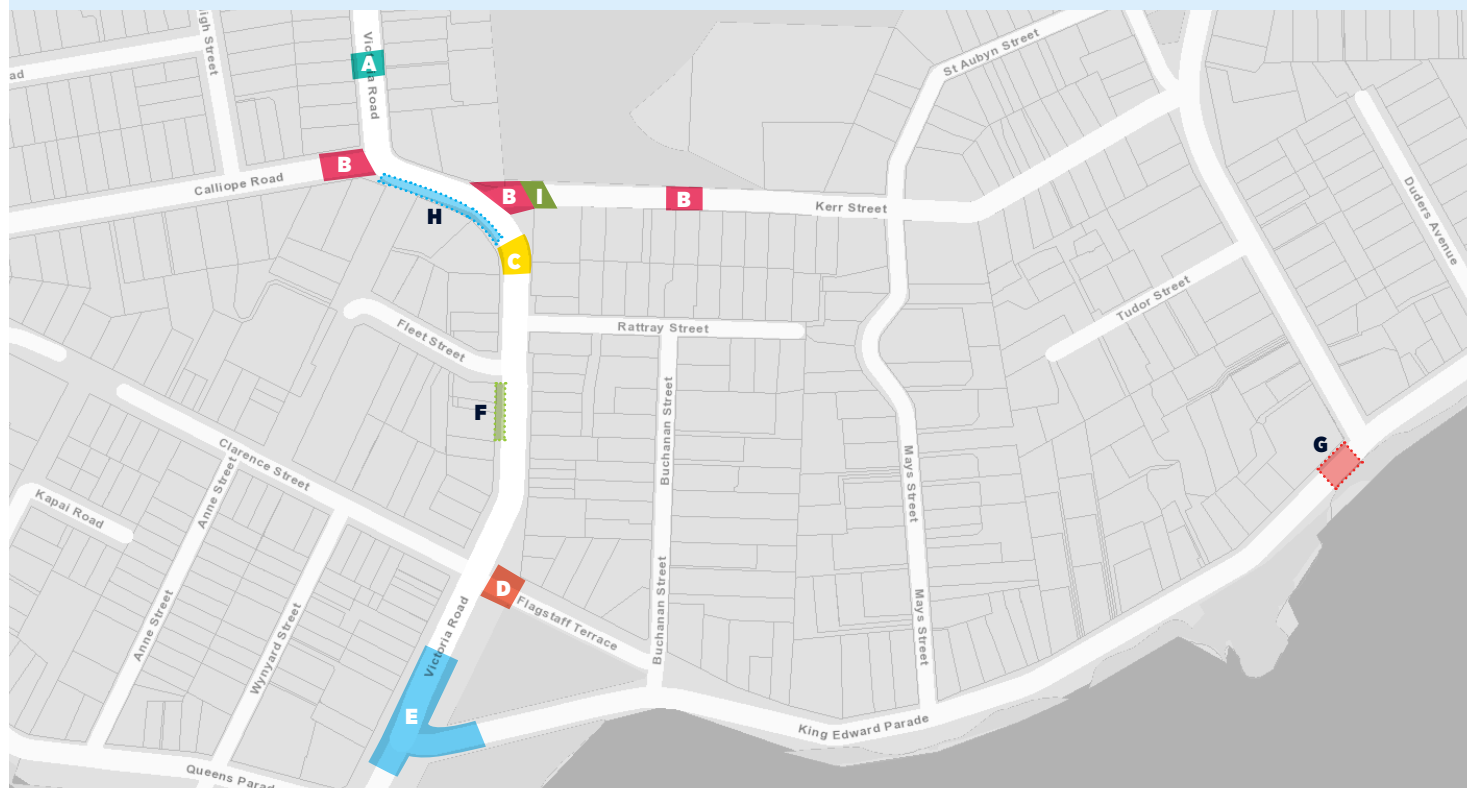

Construction Phase Map

Safety Improvements

Timeline 2023*

Construction Phases		JUN	JUL	AUG	SEP	OCT	NOV
A	Upgrade to raised crossing	✓					
B	New raised crossings		✓				
C	Street lighting						
D	New raised crossing			✓			
E	Upgrade to two existing crossings and one new raised crossing			✓	✓		
F	F1: Upgrade bus stop			✓			
F	F2: Safety barriers installation						
G	G1: New zebra crossing - refuge island	✓					
G	G2: Street lighting and landmarking						
H	New cycleway					✓	
I	Stormwater drainage improvements					✓	

*Subject to weather condition and please refer to the works notification letter for more details.



**What have
we delivered**

Phase A Victoria Road (Calliope Road to Hastings Parade) raised crossing for pedestrians and cyclists



Phase B Calliope Road and Kerr Street Raised Pedestrian Crossings





What have we delivered

Phase D Flagstaff Terrace Raised Pedestrian Crossing



Phase E Victoria Road and King Edward Parade Safety Improvements





**What have
we delivered**

Phase F Victoria Road Bus Stop Upgrade



Phase H Victoria Road Cycleway






Next up

(weather dependant)

In November, we will complete Phase F2, C of the project

Phase C Streelight upgrade

Phase F2 Safety barriers installation

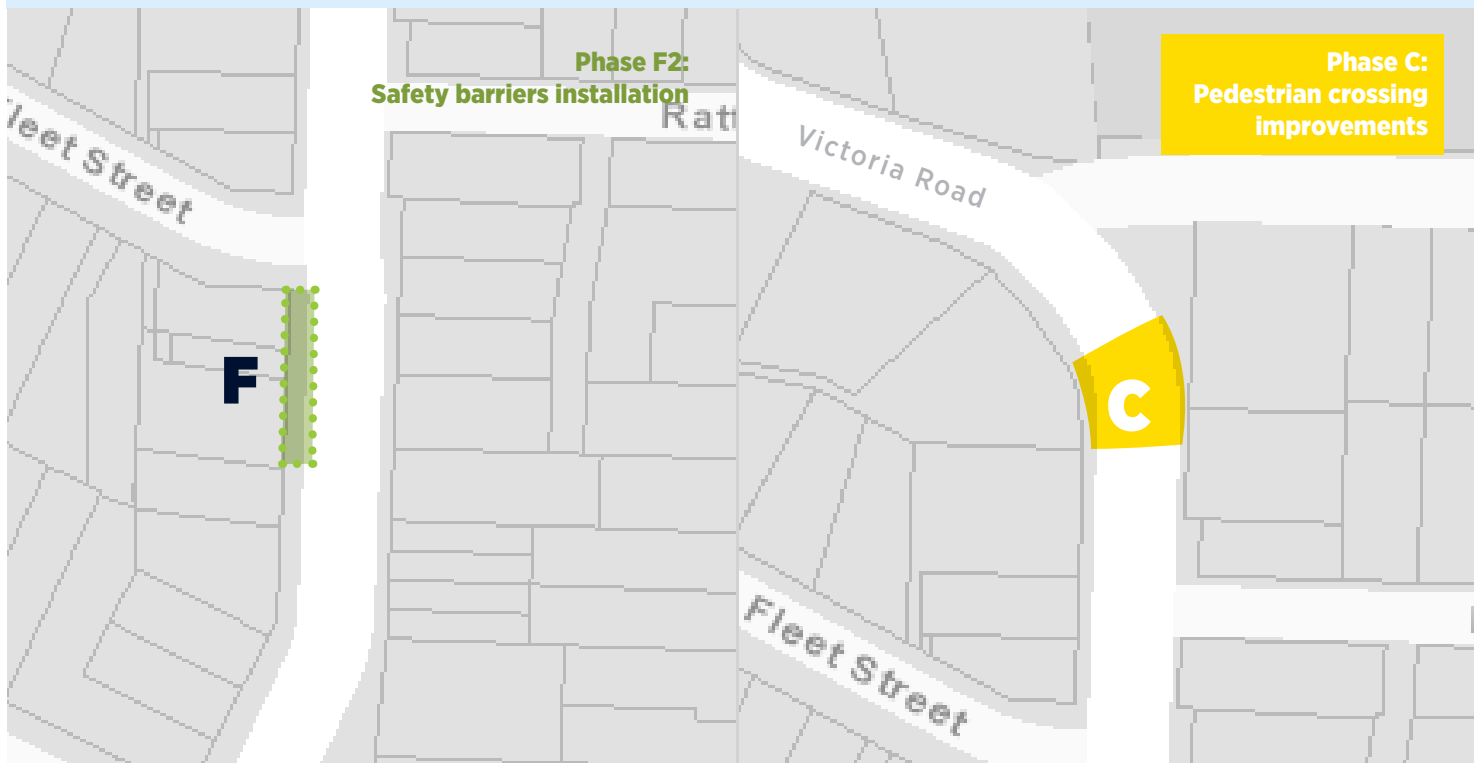

For your safety

Traffic management is in place to keep the public and our crew safe while we carry out this work. Please make sure children and pets in your care do not enter any fenced areas, and be aware of the trucks and other machinery in the area.

Pedestrians and cyclists are being diverted around our sites. Please follow our detour routes and stay safe. If you would like further information regarding the project, please contact us using the details below.

For information about construction or work sites, contact Fulton Hogan by email at Emma.Cushnie@fultonhogan.com or phone at **027 532 4305**.

For all other queries about the project, contact Auckland Transport by email at projects@AT.govt.nz or phone at **09 355 3553**.
