

Construction Update

Mission Bay | Safety Improvements


On behalf of everyone at Auckland Transport we hope this newsletter finds you and your whānau well.

Here's a quick update from the project team about the work that is happening in and around Mission Bay.

The construction of the Mission Bay Safety improvement project started on 26 April 2022 after our consultation and significant community input. We acknowledge everyone who shared their views with AT including representatives from the Business Association, Resident's Association and the Ōrākei Local Board.

We would like to thank you for your patience while this important safety work is carried out. To minimise disruption, the works will be carried out in stages. Construction phases location and timeline can be found below.

For regular updates, please visit our website: [AT.govt.nz/missionbaysafety](https://at.govt.nz/missionbaysafety) or scan the QR code.

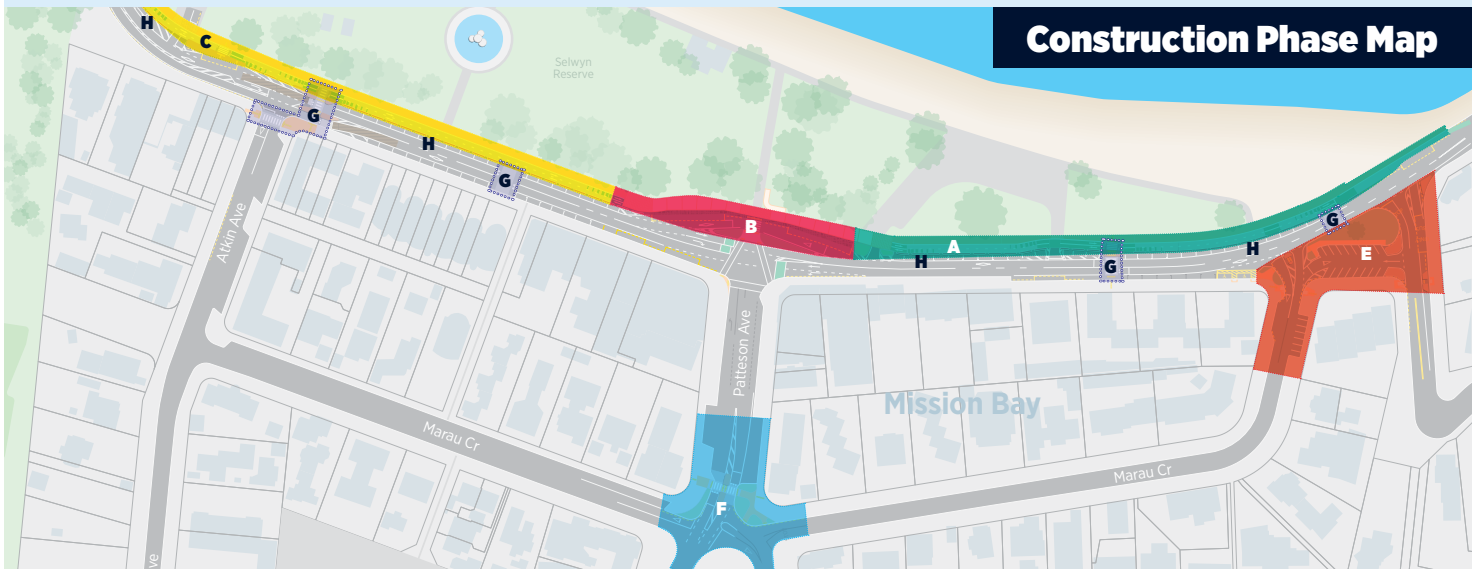

Construction Phase Map

Safety Improvements

Timeline 2022*

Construction Phases	Apr	May	Jun	Jul	Aug	Sep	Oct
A Footpath renewal and cycleway preliminary work							
B Shared path construction							
C Footpath renewal and cycleway preliminary work							
D Road resurfacing (nightshift)							
E Carpark construction							
F Intersection upgrade							
G Speed tables installation (nightshift)							
H Cycle separators installation							
I Linemarking and surfacing (nightshift)							

*Subject to weather condition and please refer to the works notification letter for more details.





What we are doing

We are building raised crossings, a separated cycleway, improving the footpath and shared space areas, upgrading intersections and parking, and making other safety improvements around the area. Significant community and technical input have been incorporated into the design of our safety project.

These improvements will slow down traffic to create an environment that is safer for everyone. Check out our staging map on the first page that shows how we will be constructing our safety improvements.

We have also tried to visualise the planned improvements through a short video clip. Please scan this QR code or click the hyperlink below to access the video.



[Reduced Speeds in Mission Bay – Existing & Proposed \(vimeo.com\)](#)

Phase C work currently in progress.





What we've been up to

Tāmaki Drive (from the town entrance/footbridge to Clock Tower) footpath renewal and cycleway preliminary work - Phase C update.

The works on first section of Phase C (from footbridge to Atkin Ave/Tāmaki Dr intersection) is well underway, and the team took advantage of the sunny weather prior to the heavy rain we have experienced lately.

We have now completed the first section of the new footpath. The asphalt has been laid, the drainage upgraded and a new kerb line installed. You may have noticed we have tied bright coloured ribbons on the lower branches of Pohutukawa trees in the vicinity of the works. This is for protection reasons and gives guidance to the crew working on the path to highlight where the branches are located.

We have also moved on to working on the second section of Phase C (from Atkin Ave/Tāmaki Dr intersection to the clocktower), where the old footpath has been removed. Once again, we'll be improving the footpath, building out kerbs and traffic islands, doing preliminary work on the cycleway and upgrading the existing drainage network.



Newly laid asphalt footpath on Tamaki Drive (first section of Phase C).



Old footpath removed on Tāmaki Drive ready for upgrade works to begin (Second section of Phase C).

Selwyn Ave/ Marau Cres Intersection Carpark Construction work - Phase E Update

With the preparation work now complete the crew is well underway constructing the new carpark during Phase E.

While this work is underway, a small part of Selwyn Avenue around our work area is currently a one-way traffic flow. Please take care while driving and follow signage carefully. These nine new carparks are due for completion at the end of August. This will increase the parking capacity in Mission Bay, especially for visitors at the Selwyn Avenue and Marau Crescent intersection.

Most of this work will be completed during the day (between 7am - 7pm). However, please keep in mind that there are some night works required for resurfacing, line marking and speed tables later in the project, which will take place between 7pm - 5am. We will confirm those dates closer to the time.



Phase E: Selwyn Avenue carpark





Next up (weather dependent)

During July and into August we will continue working on Phase C and Phase E.

Some night works would also be required toward mid-late August to complete Phase D, G, H, and I works. Night works are required to allow surfacing, linemarking, cycle separators installation works and drainage installation works which are located in the middle of carriage way. Night works are planned and required due to the nature of the works and to minimise major traffic interruptions during the day. These night works will be advised when dates are confirmed.

In each monthly newsletter we will provide more detailed information for each phase and what is happening.



Missing signs

We are sad to report that several traffic management signs that were in place for public and road user safety were stolen from the work site in the early hours of Friday 8 July (the last day of the school term). We would appreciate if you could keep an eye out for any suspicious behaviour in and around our work sites and report it to police.



For your safety

Traffic management is in place to keep the public and our crew safe while we carry out this work. Please make sure children and dogs in your care do not enter any fenced areas and that you are aware of the trucks and other machinery in the area.

Pedestrians and cyclists are being diverted through the park and along the waterfront path. Please follow our detour route and stay safe.

Get in touch

We have a fortnightly drop-in space outside Mövenpick where you can get up to date information about the project or come and chat to us. Auckland Transport and Fulton Hogan project staff will be available every second Friday to answer your queries about the works (dependent on weather and staff being well during the winter months). Our next two drop-in sessions will be held on the 12th and 26th of August from 1- 2pm. Please stop by and say hello if you are in the area at this time. We'd love to chat to you.



Friendly faces at the Friday drop in session

For questions about construction activities (machinery, traffic management etc.) contact Fulton Hogan Stakeholder Manager, Linda Casey on **0800 348 007** or email Linda.Casey@fultonhogan.com
For project related questions, please contact AT on **09 355 3553** or email projects@AT.govt.nz

