



Links to GI Cycleways

May construction update

In this update we want to give you a quick summary of our progress since March, and how the works at the Glen Innes Town Centre are coming along.


We have also started working at the Stonefields Avenue and College Road intersection.

Glen Innes Town Centre progress

Businesses have raised concerns about disruptions and access for customers, so we worked with Downer to reduce the impact of our works.

We have split the works on the eastern side of Apirana Avenue into stages 3 and 4 which allow us to keep access to parking available. While we're working on stage 3, access to shops will be maintained.

We understand that our works can be noisy and dusty, so we're working as quickly and safely as can.

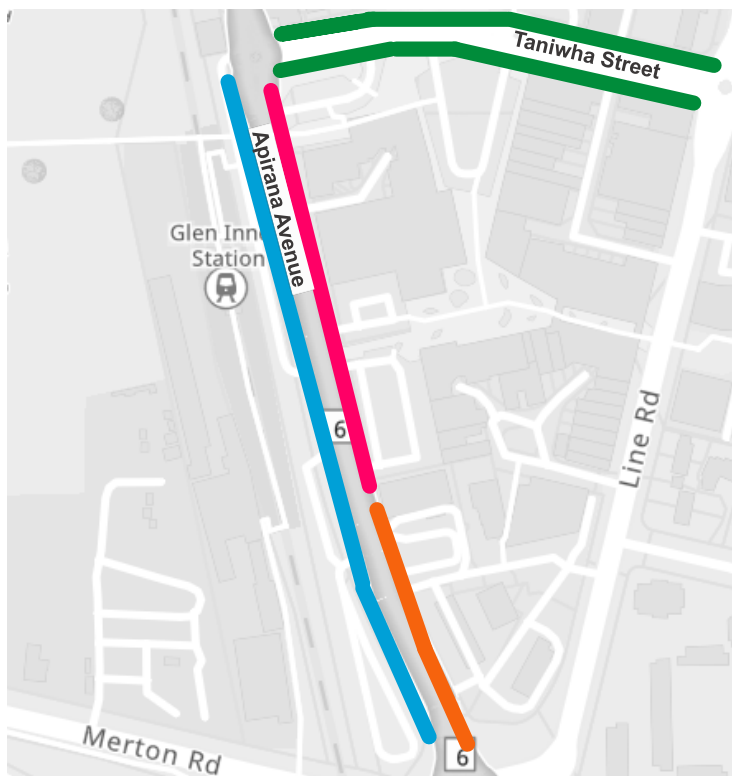

- Stage 2** – Footpath completed
- Stage 3** – In progress
- Stage 4** – We plan to start works in late May
- Taniwha Street** – We plan to start works in July

Apirana Avenue stage 2

The footpath on the western, train station side, is now complete.

To finish the cycleway we need to install the concrete separators, asphalt the road, and paint permanent road markings.

We will do this at night once all the changes in the town centre have been completed.





Apirana Avenue stage 3

We have made excellent progress and have completed:

- 80% of kerb and channel works
- 90% of excavation works
- 80% of drainage works
- Half of the pedestrian crossing connecting shoppers to the train station

We now need to install Chorus power ducts, concrete foot paths, and streetlights.



Stonefields Avenue and College Road intersection

We have also started working at the Stonefields Avenue and College Road intersection to prepare for the cycleway as well as doing routine road maintenance to keep the road in a good condition.

We have completed 80% of the drainage works as well as 50% of the excavation works needed to install the raised crossings, kerb and channel, and footpaths.



Upcoming works

Apirana Avenue stage 4

We plan to start working on stage 4 in late May, which includes kerb and channel, and footpath works. It can get noisy and dusty so we are aiming to work outside of core business hours as much as we can.

While we work on stage 4, we will continue to provide businesses are open signs and keep the footpath open during the day for customers.

We want to thank the Glen Innes community for their patience whilst we complete these works.

Want to get in touch?

For general project enquiries email projects@at.govt.nz or phone 09 930 5090

For more information about the project visit at.govt.nz/links2GI

