


Neville St Rehab

Programme / Methodology / Staging

Start: Mid April

Approx 2-3 Weeks

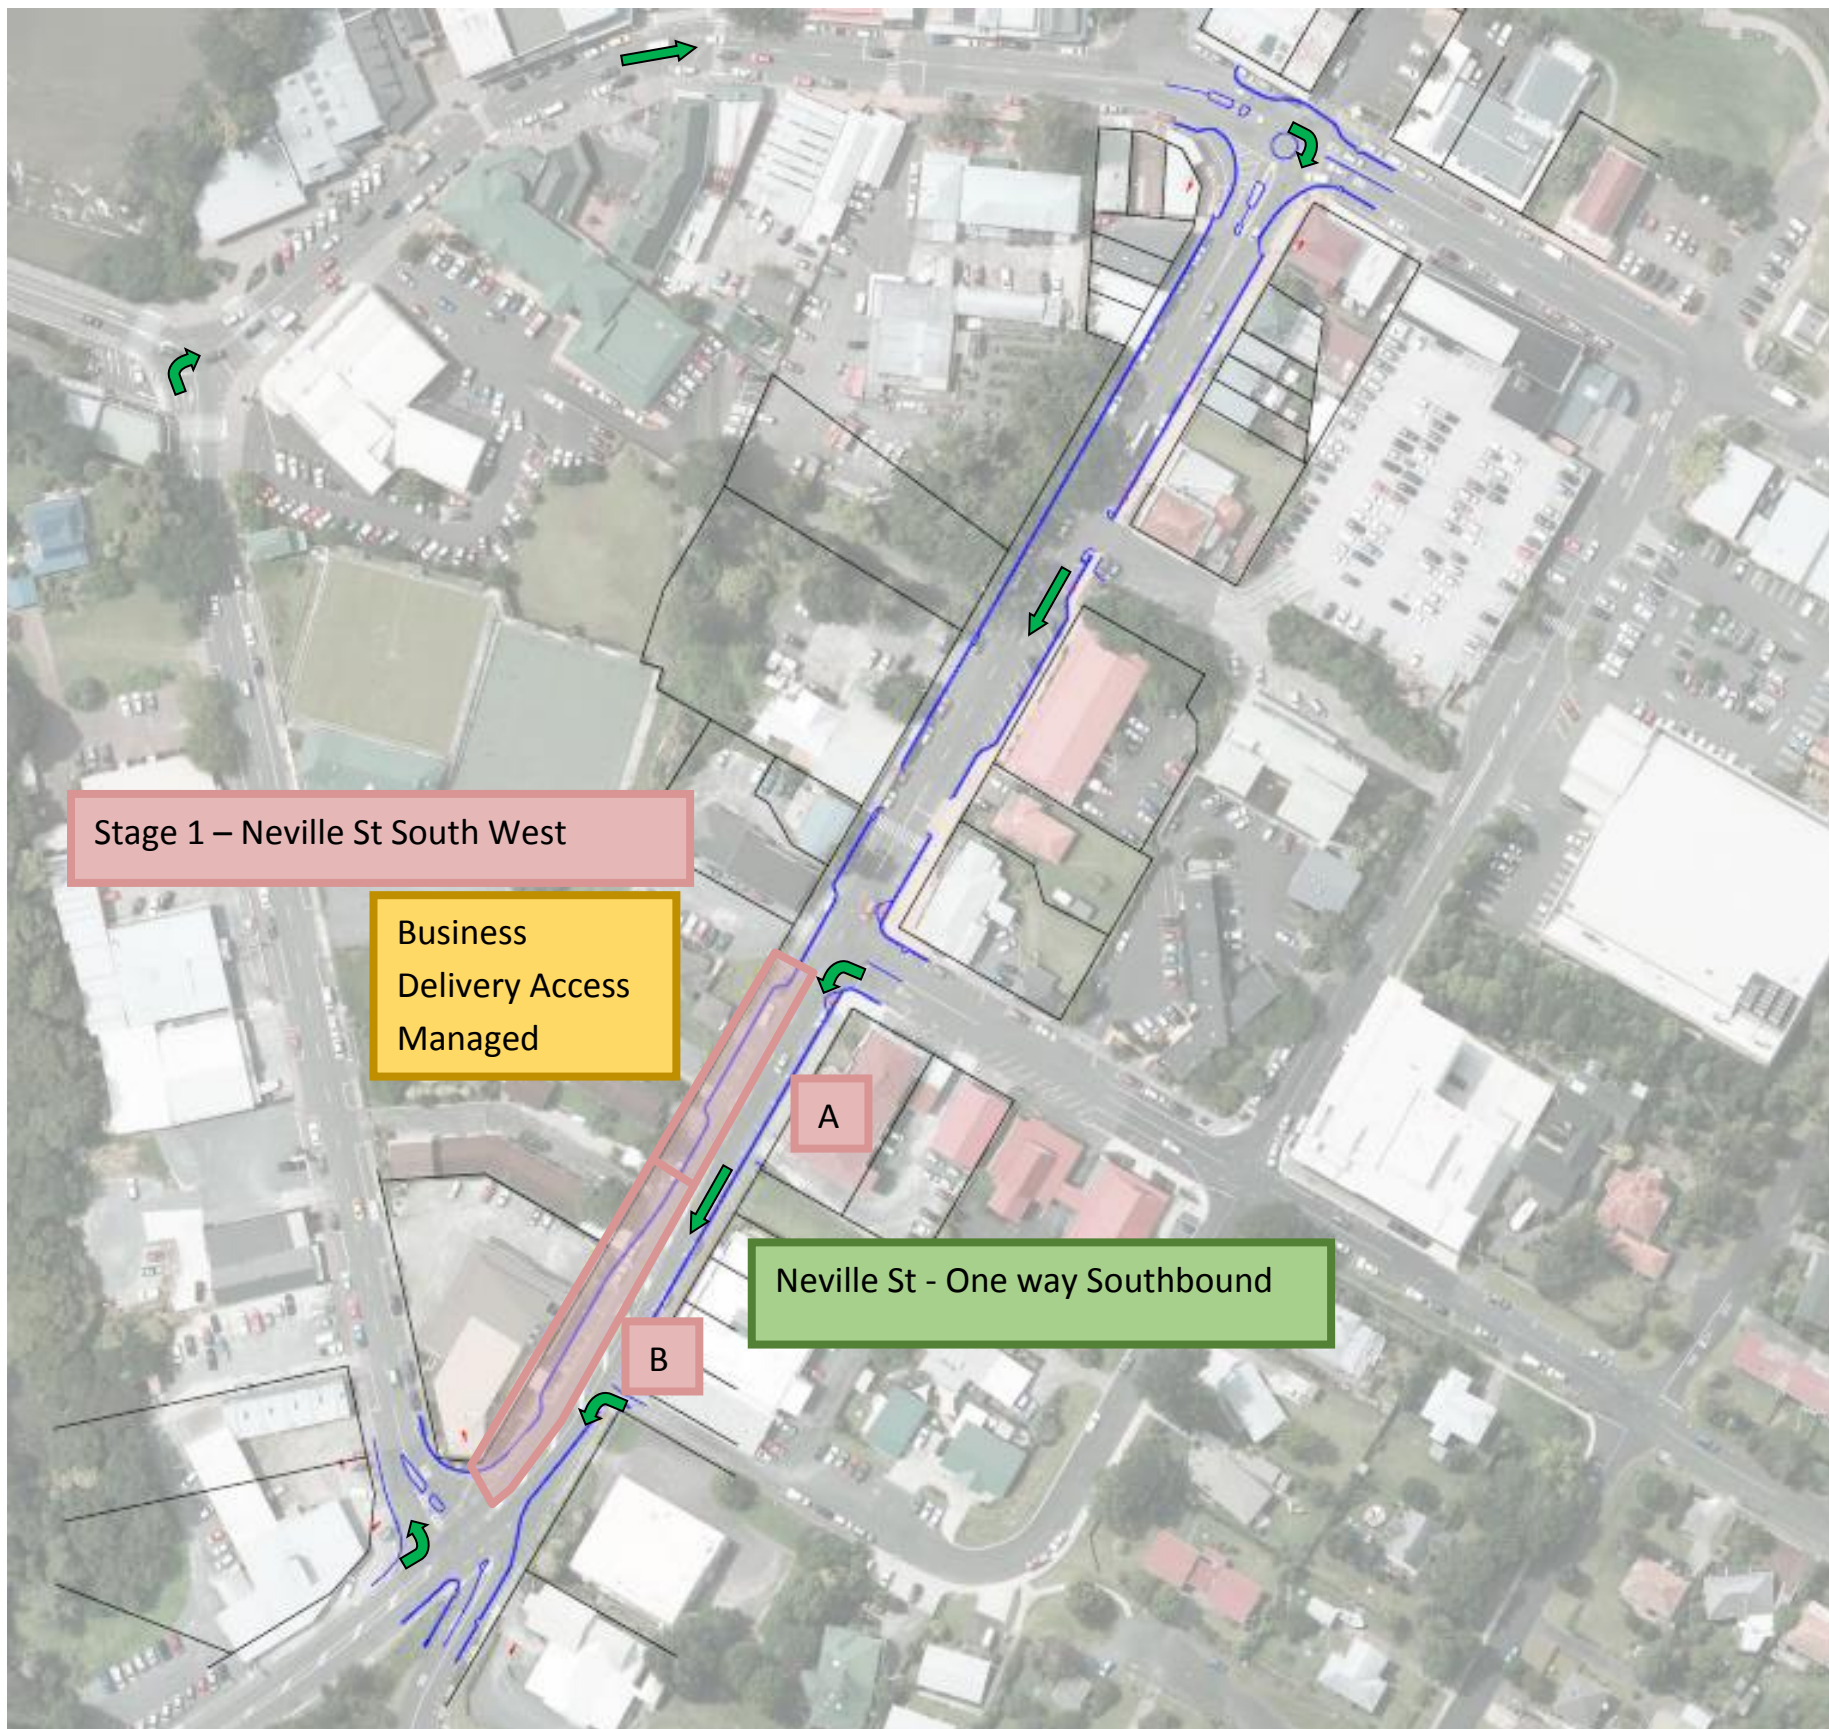

Stage 1 – Neville St South West

- Service Locate and hydro excavation
- Drainage works
- Road Pavement excavation
- Road Pavement buildup
- Chipseal

Notes:

- Service locate and drainage works completed under isolated traffic control
- Neville St Carparks closed for Road Pavement works
- Section A completed and carparks reinstated then Section B
- Neville St closed to northbound traffic between Mill Ln and Alwick St
- Business delivery access managed
- Pedestrians to use either footpath

Neville St Rehab

Programme / Methodology / Staging

Start: Early May Approx 2-3 Weeks



Stage 2 – Neville St South East

Service Locate and hydro excavation

Drainage works

Kerbing

Road Pavement excavation

Road Pavement buildup

Chipseal


Notes:

- Service locate and drainage works completed under isolated traffic control
- Neville St Carparks closed for Road Pavement works
- Section A completed and carparks reinstated then Section B
- Neville St closed to Southbound traffic between Mill Ln and Alnwick St
- Pedestrians to use Western footpath
- Morpeth St Closed at Neville St

Neville St Rehab

Programme / Methodology / Staging

Start: Early May Approx 2-3 Weeks

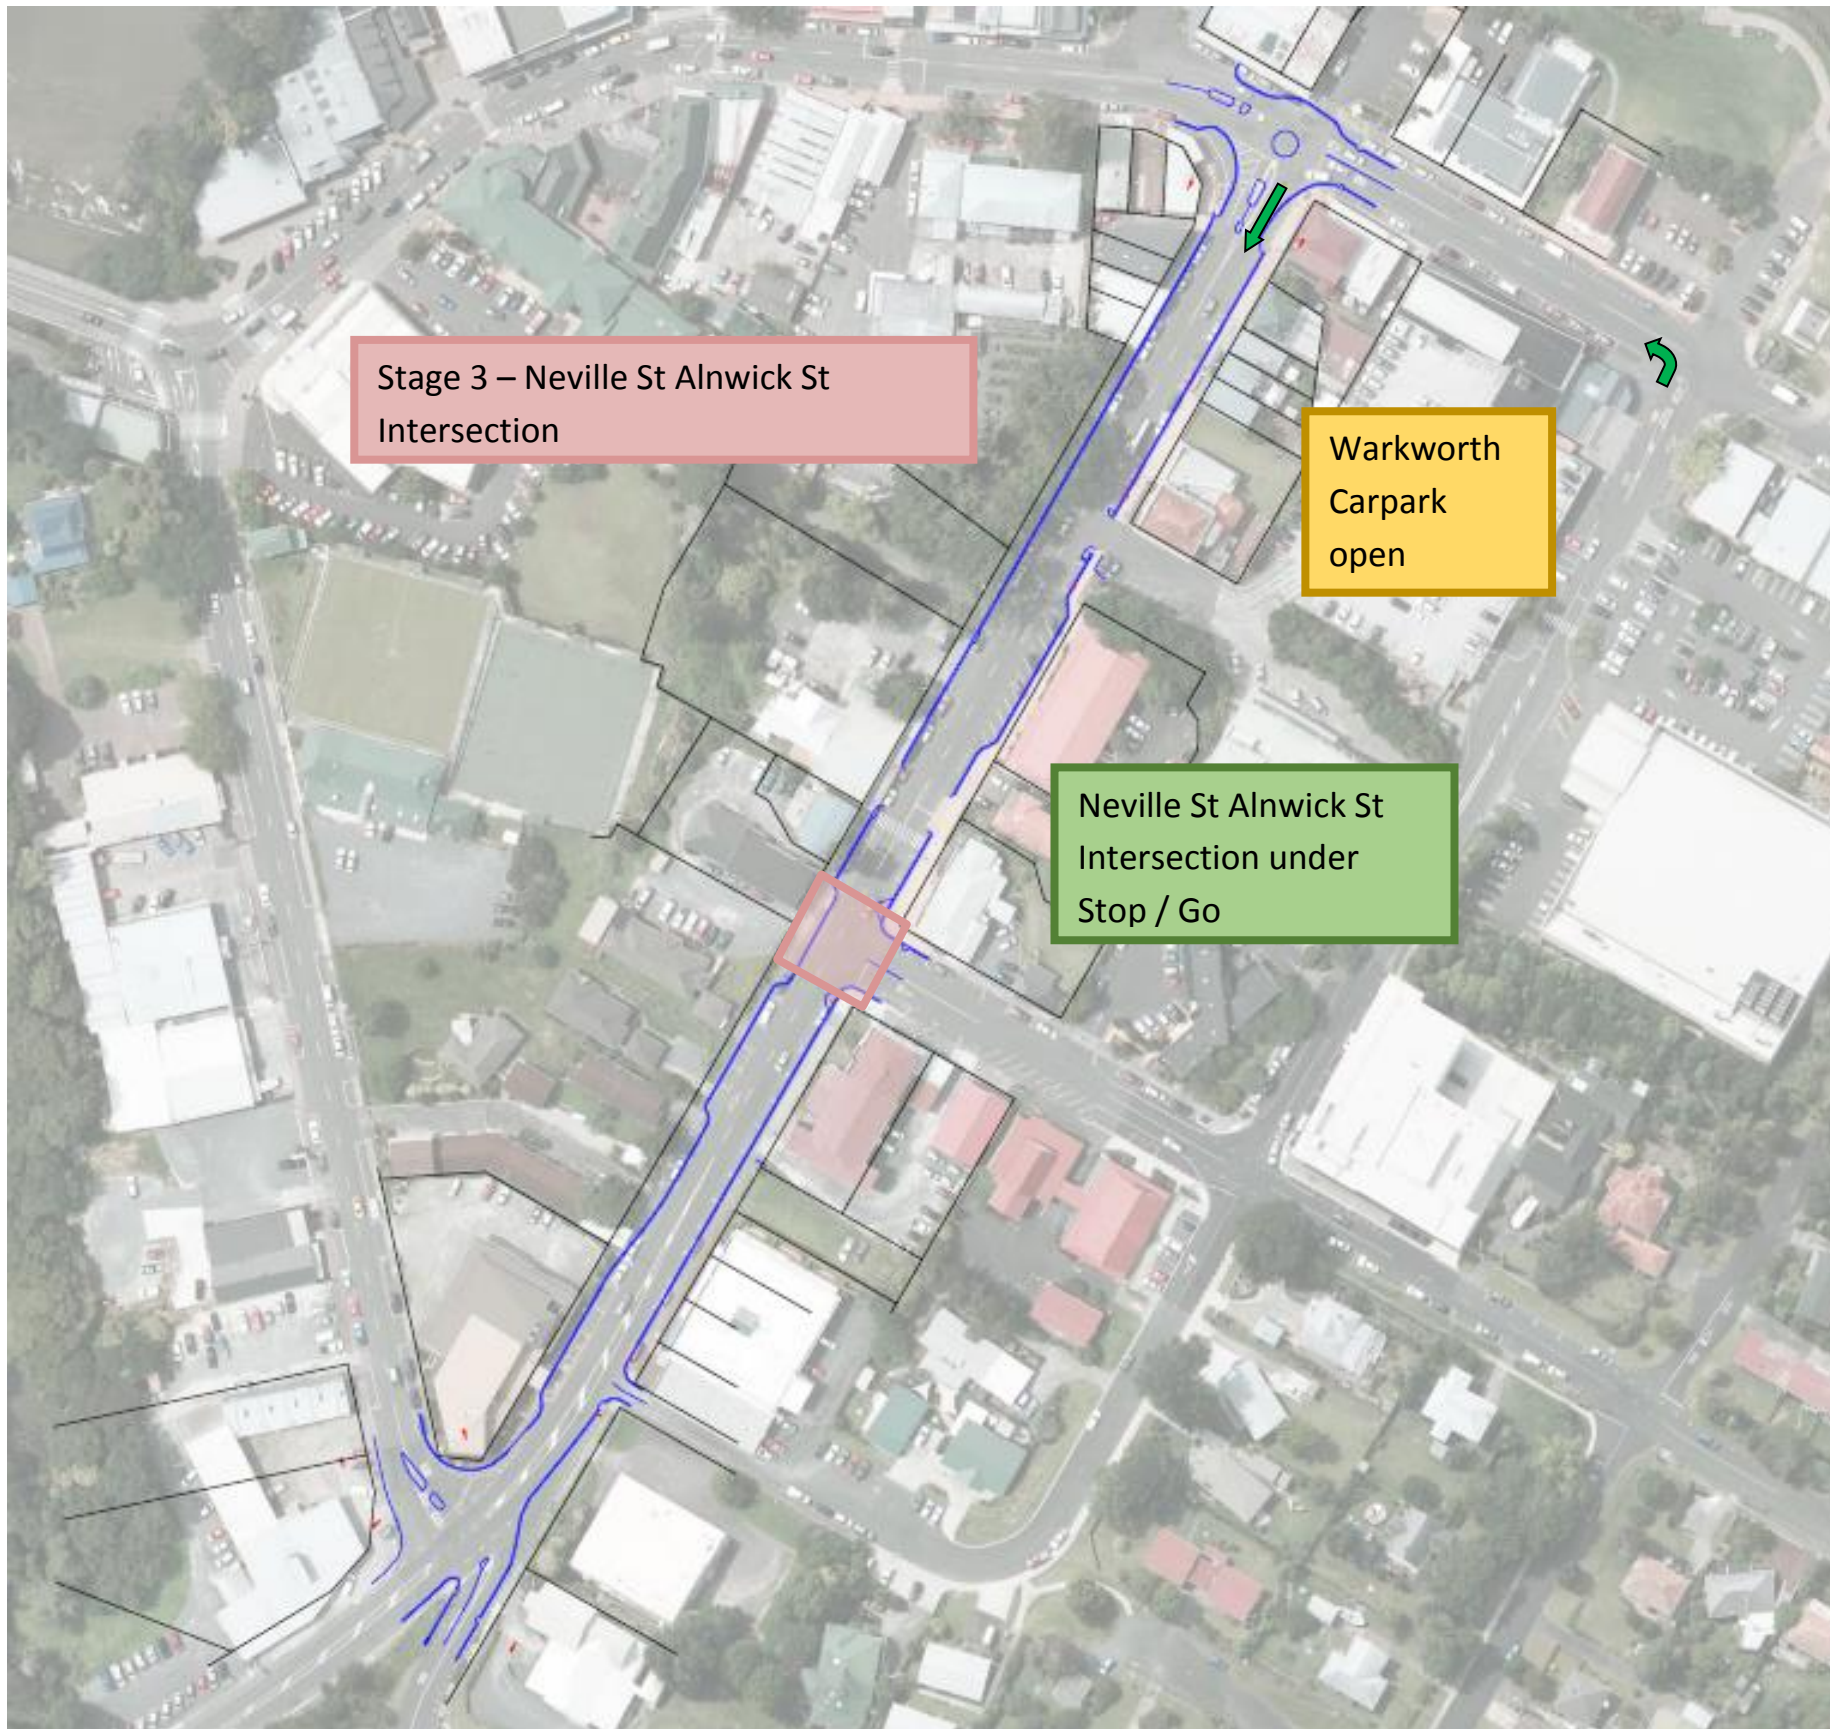

Stage 3 – Neville St Alnwick St Intersection

Warkworth Carpark open

Neville St Alnwick St Intersection under Stop / Go

- Stage 3 – Neville St Alnwick St Intersection**
- Service Locate and hydro excavation
 - Drainage works
 - Road Pavement excavation
 - Road Pavement buildup
 - Chipseal

Notes:

- Road Pavement works completed as part of stage 2
- Intersection works under Stop / Go to avoid Road Closure



PO Box 102, Wellsford 0940
New Zealand
Ph 09 423 6000
Fax 09 423 6041
www.wharehine.co.nz

Title:
Neville St Rehab – Stage 3 Neville St Alnwick St Intersection
Programme / Methodology

Notes:


Job No.	
Sheet.	3 of 8
Scale.	N.T.S
Date.	December 2017

Neville St Rehab

Programme / Methodology / Staging

Start: Late May

Approx 1-2 Weeks

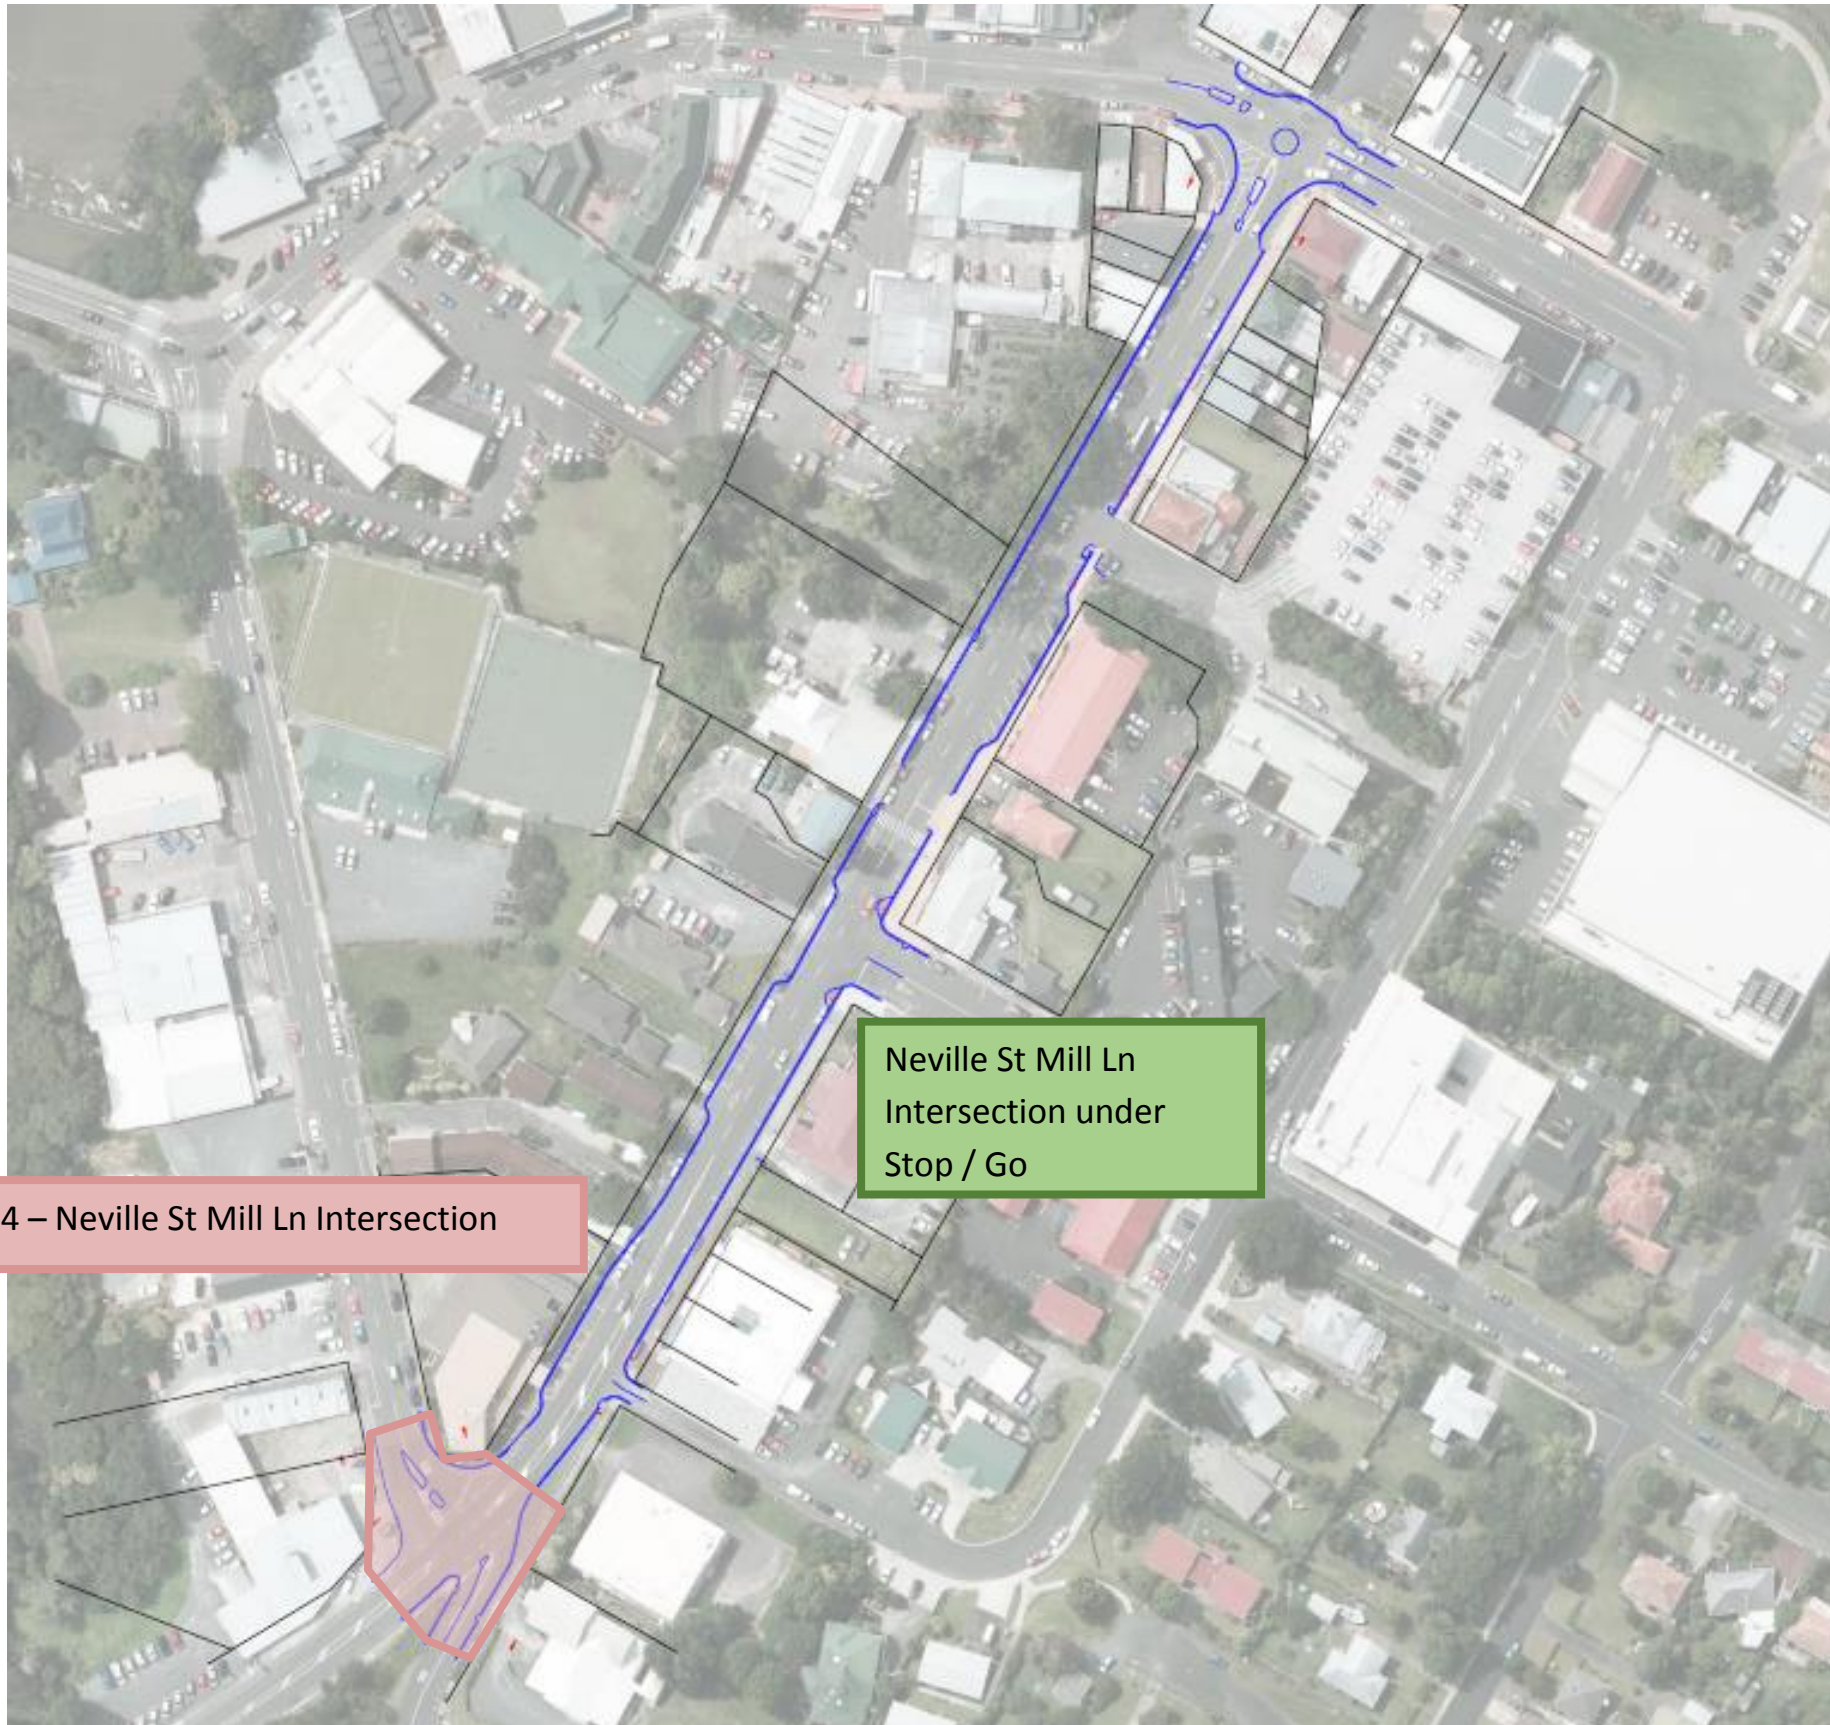

Stage 4 – Neville St Mill Ln Intersection

Stage 4 – Neville St Mill Ln Intersection

Service Locate and hydro excavation

Road Pavement excavation

Road Pavement buildup

Chipseal

Notes:

- Service locate and drainage works completed under isolated traffic control
- Pedestrians to use either footpath
- Intersection works under Stop / Go to avoid Road Closure

Neville St Rehab

Programme / Methodology / Staging

Start: Late May Approx 3-4 days



Stage 5 – Surfacing

- AC
- Linemarking
- Landscape
- Tidy

Notes:

- Works under Stop / Go to avoid Road Closure.
- Night Works



PO Box 102, Wellsford 0940
New Zealand
Ph 09 423 6000
Fax 09 423 6041
www.wharehine.co.nz

Title: Neville St Rehab – Stage 5 Surfacing Programme / Methodology
--


Notes:

Job No.	
Sheet.	5 of 8
Scale.	N.T.S
Date.	December 2017

Neville St Rehab

Programme / Methodology / Staging

Start: Early June Approx 2-3 Weeks

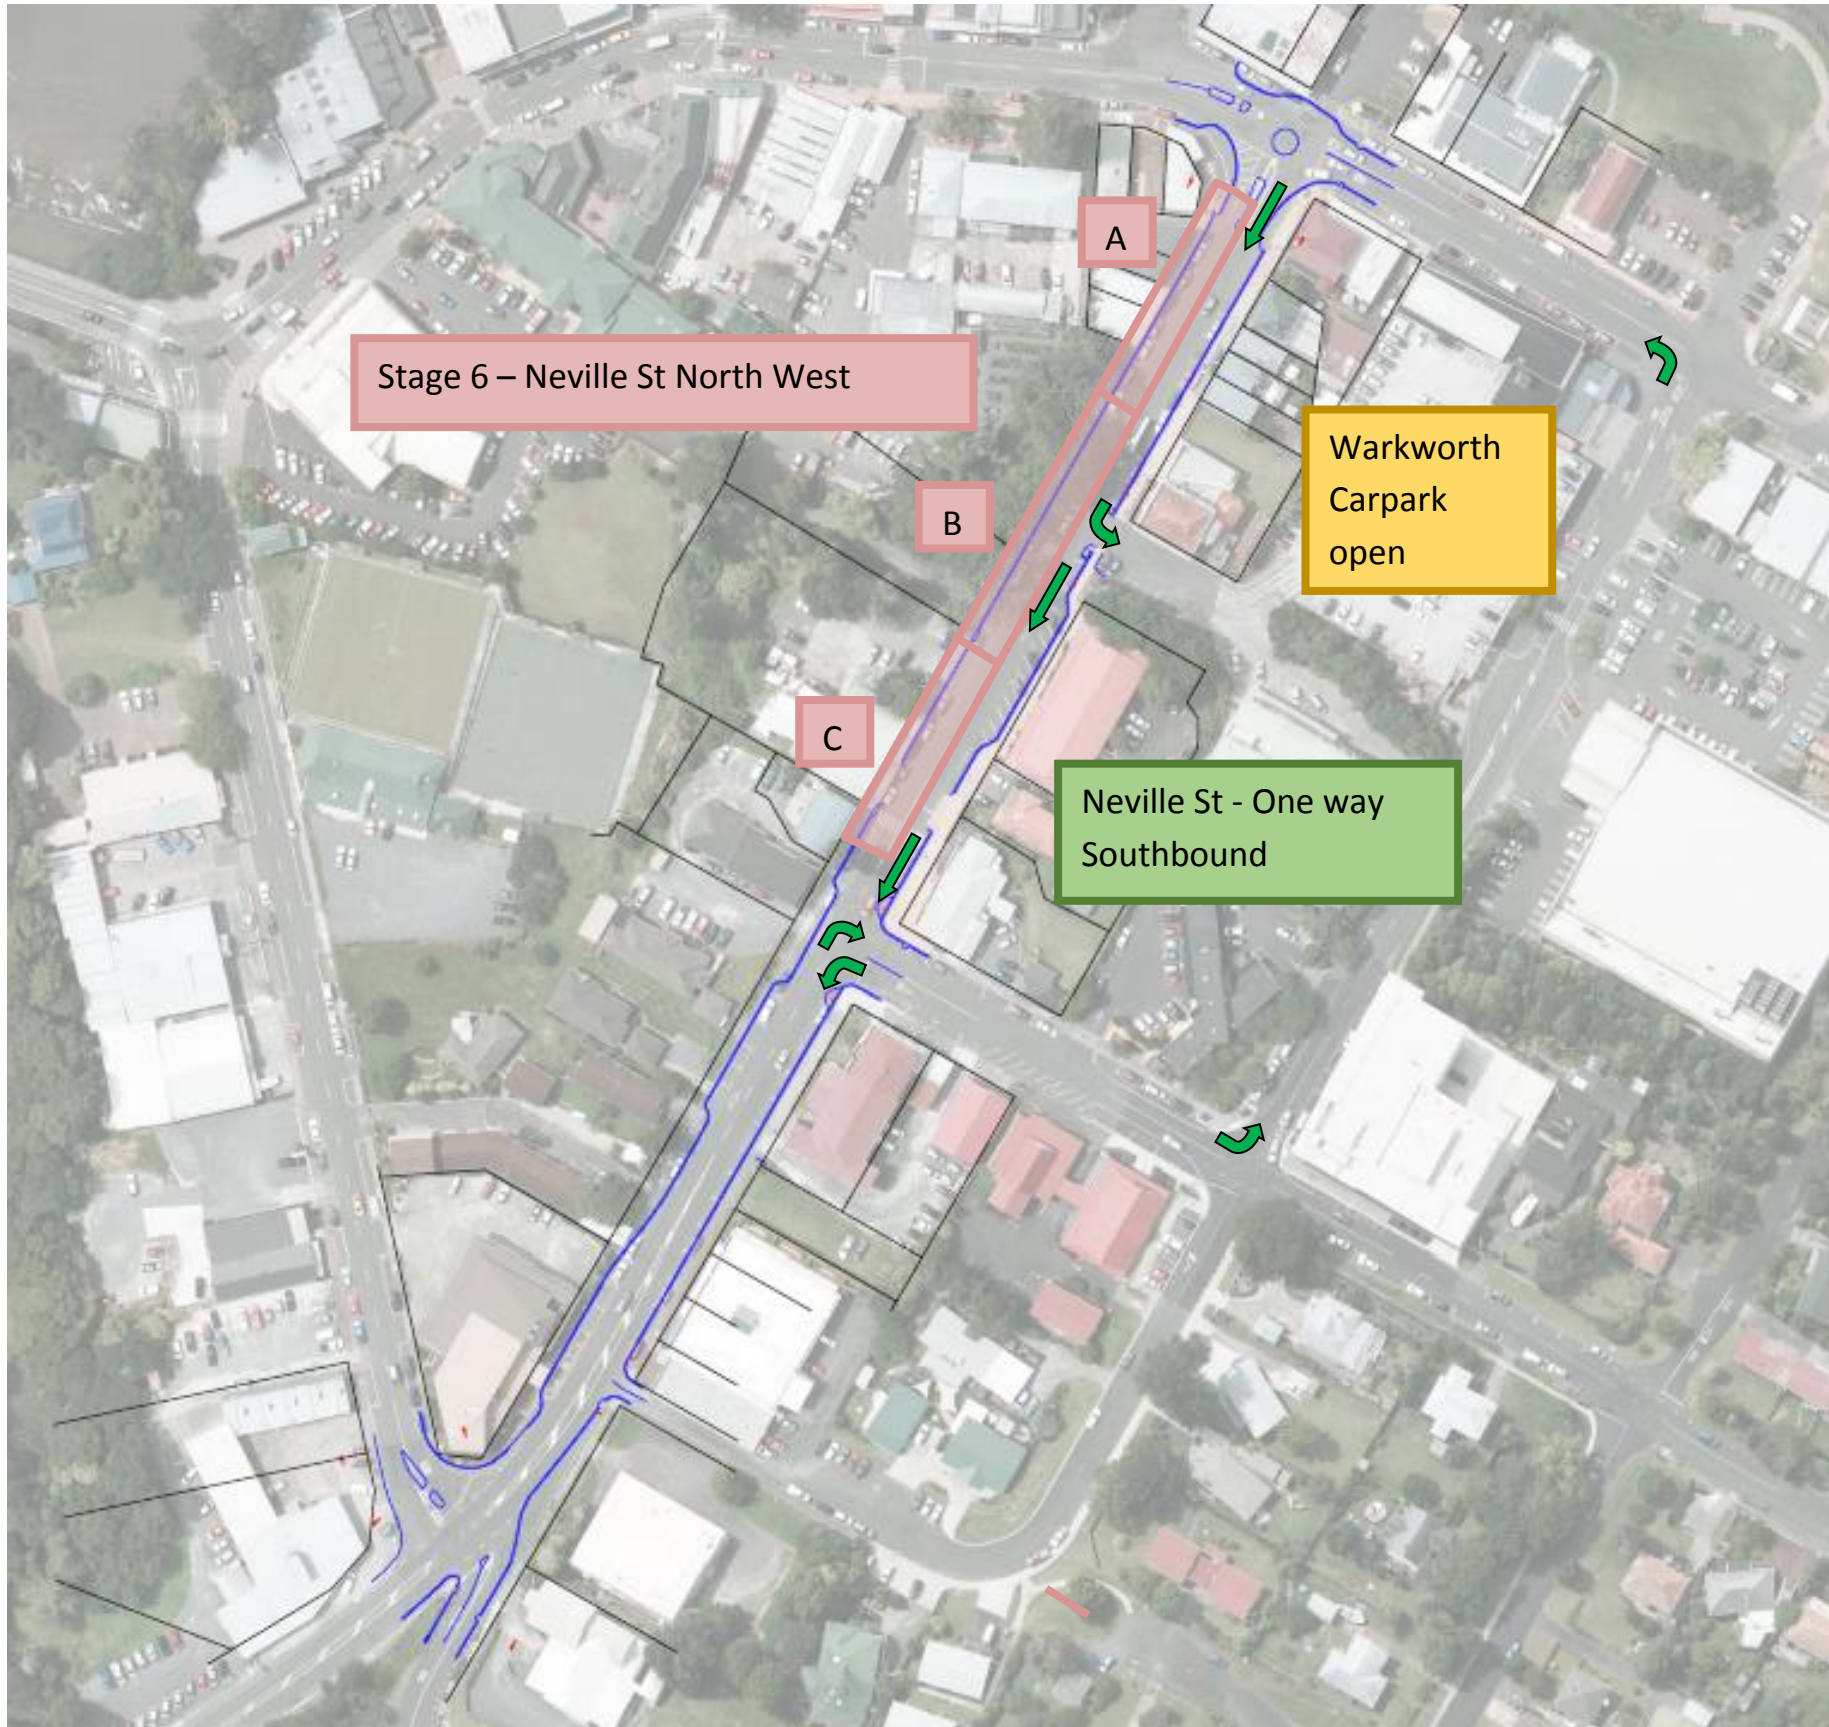

Stage 6 – Neville St North West

- Service Locate and hydro excavation
- Drainage works
- Kerbing
- Road Pavement excavation
- Road Pavement buildup
- Chipseal


Notes:

- Service locate and drainage works completed under isolated traffic control
- Neville St Carparks closed for Road Pavement works
- Section A completed and carparks reinstated then Section B then Section C
- Neville St closed to northbound traffic between Queen St and Alwick St
- Warkworth carpark Open
- Pedestrians to use eastern footpath

Neville St Rehab

Programme / Methodology / Staging

Start: Mid June Approx 2 Weeks

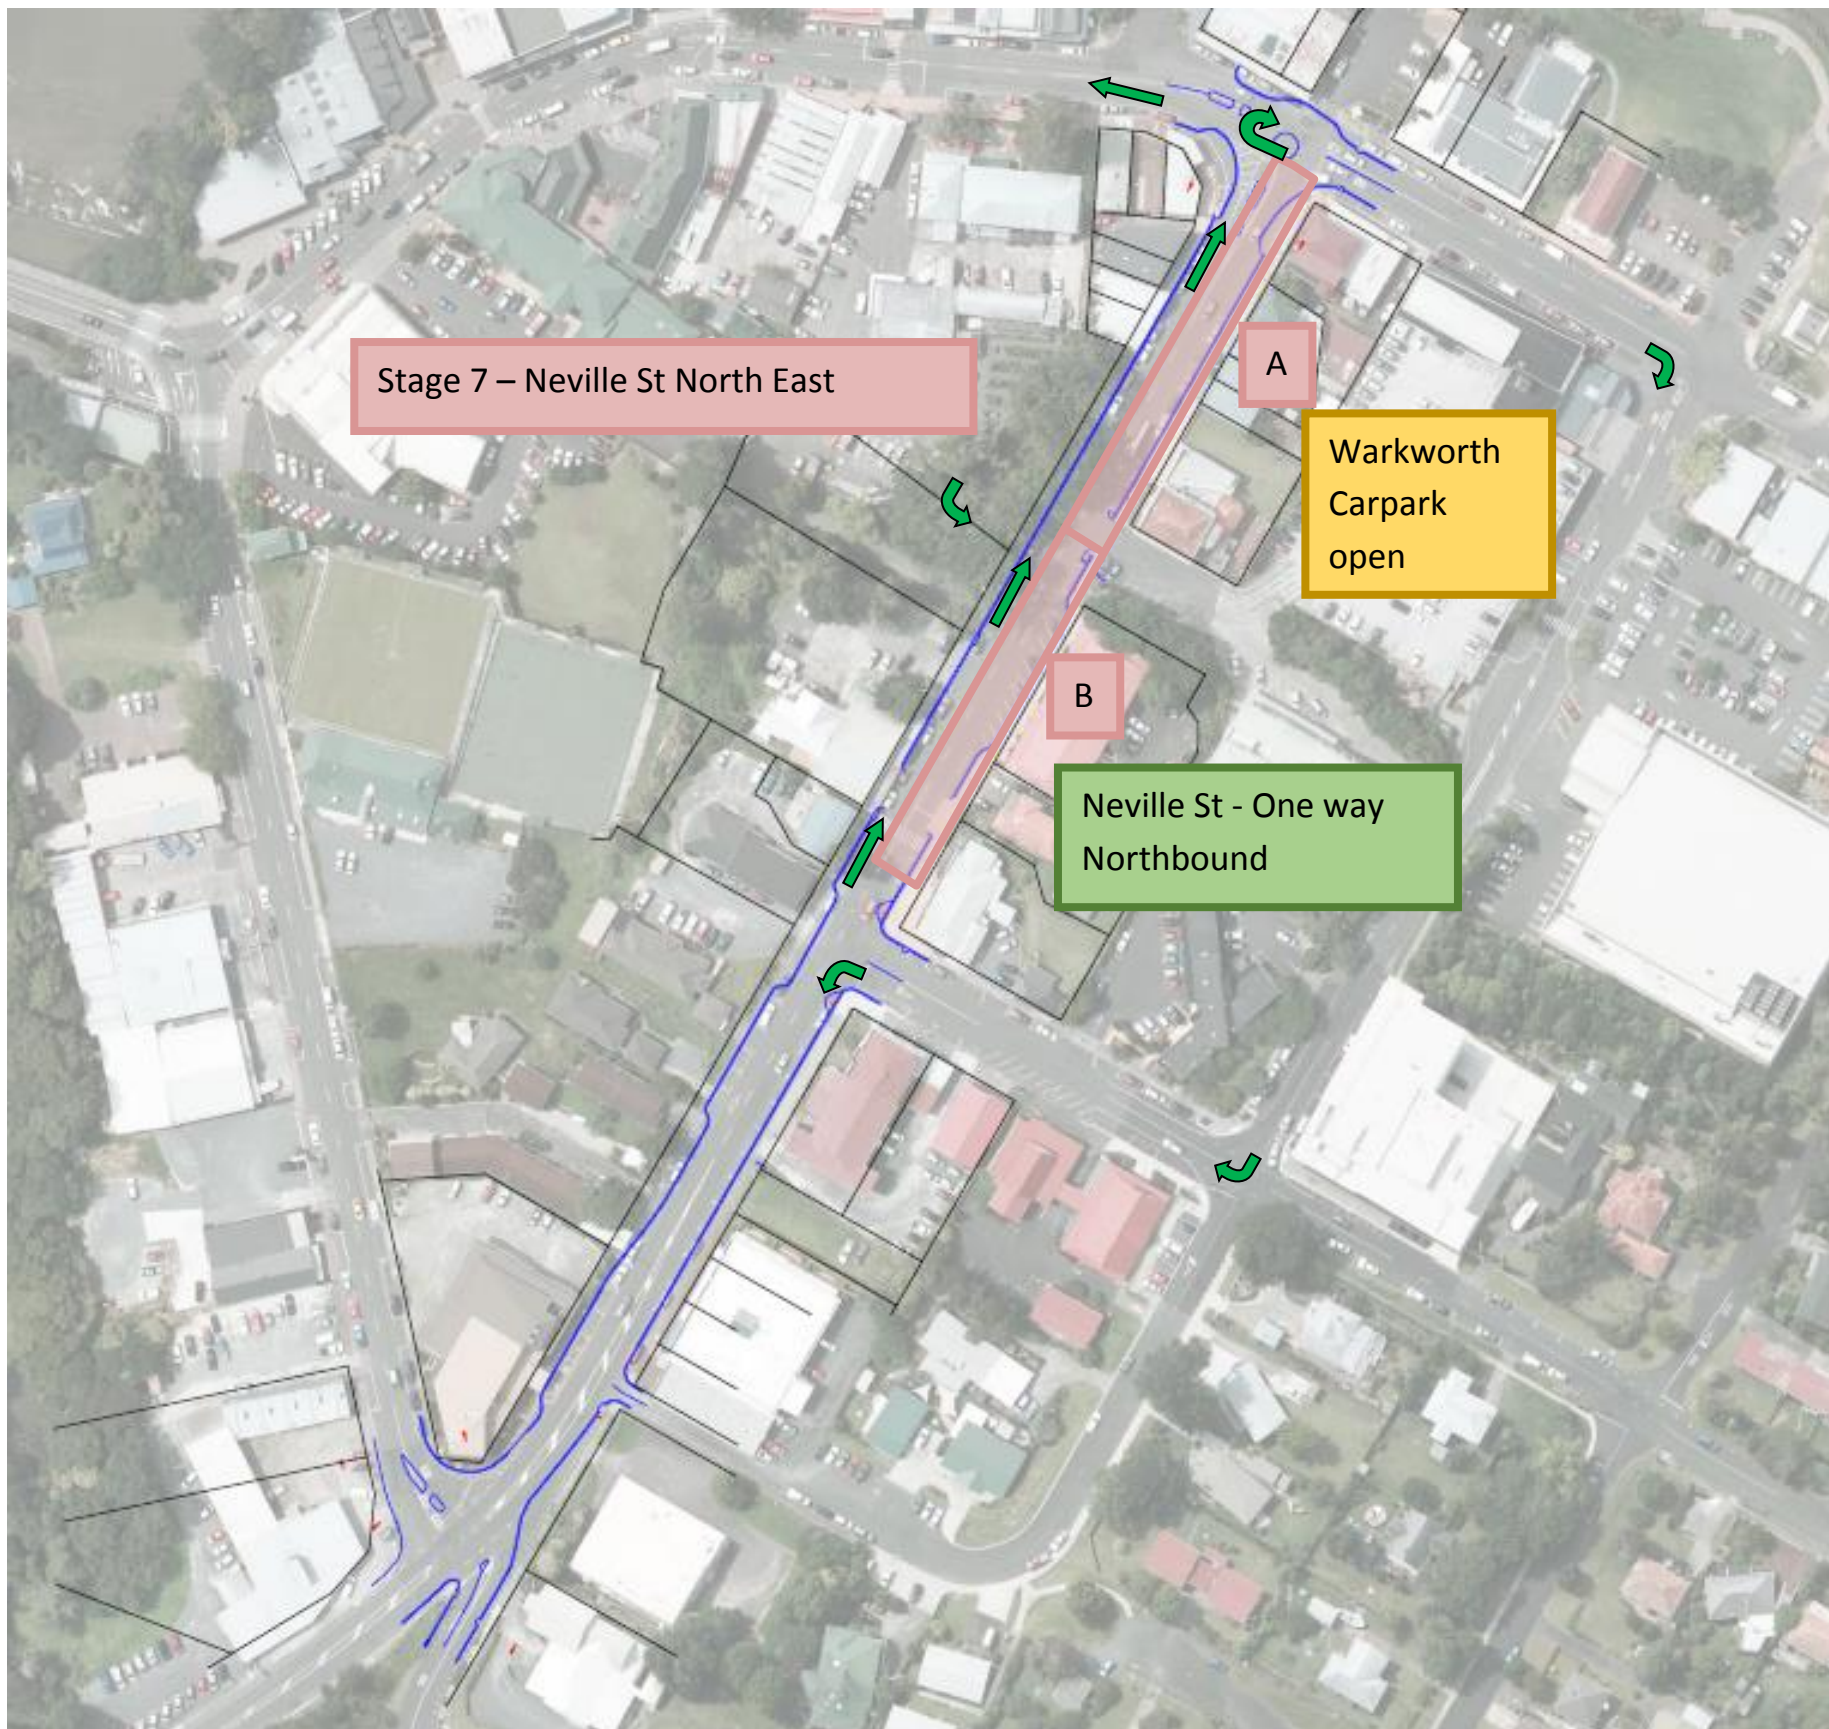

Stage 7 – Neville St North East

- Service Locate and hydro excavation
- Drainage works
- Road Pavement excavation
- Road Pavement buildup
- Chipseal

Notes:

- Service locate and drainage works completed under isolated traffic control
- Neville St Carparks closed for Road Pavement works
- Section A completed and carparks reinstated then Section B
- Neville St closed to southbound traffic between Queen St and Alwick St
- Warkworth carpark entrance closed at isolated times
- Pedestrians to use either footpath

Neville St Rehab

Programme / Methodology / Staging

Start: Late June Approx 2-3 Days



Stage 8 – Surfacing

- AC
- Linemarking
- Landscape
- Tidy

Notes:

- Works under Stop / Go to avoid Road Closure.
- Night Works
